Week 8: Midpoint Demonstration, Progress Review, and Revised Plan

Built for Cars, Deadly for Walkers: mining the roadway conditions behind Florida's pedestrian deaths, 2020–2024

Yelysei Shkirpan · Capstone Project, B.S. Data Science · Eastern Florida State College · October 11, 2026

Repository: https://github.com/Sor1na/florida-pedestrian-patterns

What this submission is. A recorded five-to-seven-minute demonstration of the end-to-end pipeline on the real files (submitted in Canvas) plus this document, which maps every required item to its evidence in the repository, compares progress against the approved proposal, and revises the plan for Weeks 9–14. The pipeline itself, its gates, logs, rerun behaviour and recovery procedures are the Week 7 deliverable (`Week7_Pipeline_Shkirpan.pdf`); this document does not repeat them, it points into them.

Required item	Where
1. Recorded end-to-end demonstration	the video, submitted in Canvas: the run and rerun of Week 7 §6.1 on the real files, the failure logs, and both traces of **section 6**
2. Architecture and lineage diagram, source → database	**section 2**: `pipeline.png` and the lineage table (Week 7, section 1)
3. Ingestion, validation, cleaning, transformation, loading procedures	**section 3** (one table pointing to the code and the Week 6–7 documents)
4. Before/after row counts, quality checks, rejected records, transformation log	**section 4**
5. Scheduling/execution, run IDs, logs, rerun, recovery tests	**section 5**
6. Trace of one normal record and one edge case	**section 6**: `evidence/week8/trace_normal.log`, `trace_edge.log`, tool `pipeline/trace.py`
7. Progress against the proposal, approved changes	**section 7**
8. Prioritized risk register and revised Weeks 9–14 schedule	**sections 8–9**
9. Runnable code and supporting evidence	the repository itself; build and run commands in Week 7 section 6.1 and the README; CI runs everything on each change

---


1. State of the pipeline at midpoint

Eleven stages, six validation gates, one-transaction loads, rerun-safe by design; merged to `main` in PR #1 and tagged `week7-pipeline`. Evidence recorded from the committed code: six scenarios, 19 of 19 automatic scenario checks pass (`docs/evidence/week7_synthetic/`); GitHub

Actions re-runs the Week 4–5 tests, all six scenarios and, from this submission on, both record traces, on every pull request and every push to `main` (`ci.yml`); the Week 7 run is green, and this package's pull request runs the suite again, traces included.

Committed evidence uses **synthetic inputs** in the FARS layout, because real FARS rows describe real deaths and stay out of the public repository (proposal, ethics section). The real 2020–2024 files are pinned by SHA-256 in `pipeline/sources.csv`; the recorded demonstration runs the pipeline on them locally, which is the first real-data execution, and the same scenario runner writes masked evidence to `docs/evidence/week7/`.

2. Architecture and lineage

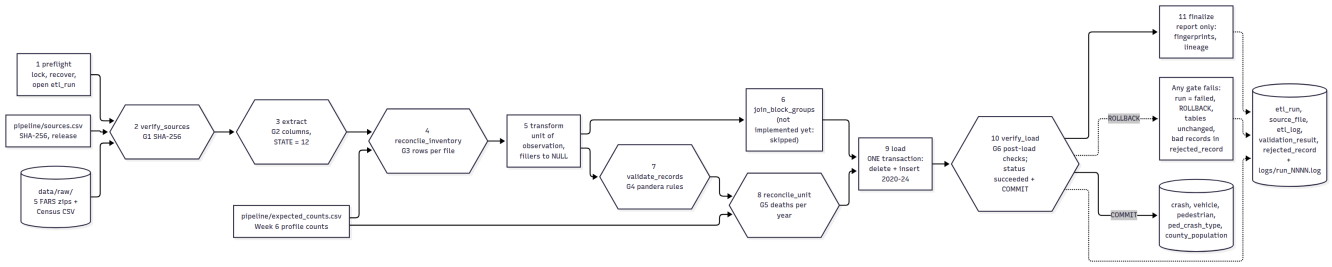

Source → database in one picture (source: `pipeline.mmd`): pinned raw files and the two control files enter on the left; hexagons are gates; the load and its post-load verification are one transaction; every run leaves bookkeeping rows and a log file whether it succeeds or fails. The full lineage table (file → member → filter → table, with the Week 6 profile counts and the synthetic run counts side by side) is Week 7, section 1; the per-year lineage lines of the latest load are printed by stage `finalize`.

3. Procedures

Procedure	Where it runs	Written down in
Ingestion (pinned download set, integrity)	stages 1–3, gates G1–G2	Week 7 §1; Week 6 §1 (what was downloaded, encodings)
Validation (structure, inventory, record rules, totals, post-load)	gates G2–G6; pandera schemas in `etl.py` `raw_schema` / `unit_schema`	Week 7 §1, §4; Week 6 §4 (the rules the gates implement)
Cleaning (what changes and what never does)	stage 5	Week 6 §4 (five issues, fixed before any transformation); Week 7 §1 stage table
Transformation (unit of observation, discretization)	stage 5 + view `v_ped_transactions` (`04_views.sql`)	Week 6 §4 issue 4 (bins fixed in advance); Week 5 design
Loading (replace-by-year, one transaction, triggers)	stages 9–10	Week 7 §1, §3

4. Row counts, quality checks, rejected records, transformation log

Before/after counts. Real files (measured in Week 6, enforced by G3/G5 on every load) and the committed synthetic run side by side:

Step	Real (expected)	Synthetic run 1 (recorded)
person rows, Florida → pedestrian fatalities	41,133 → 3,736 (by year 695/819/780/774/668)	3,394 → 596
accident rows, Florida → crashes with a pedestrian death	15,959 → 3,690	1,304 → 547
pbtype rows, Florida → typing records	5,193 → 3,736	876 → 596
census rows → county × year	3,195 → 335 (67 × 5)	79 → 67 → 335
deaths → analysis view (urban, non-freeway)	3,736 → 3,053	596 → 499
load, rerun	every year "deleted N, inserted N", fingerprint unchanged	same, `c0656528b64a…`

Quality checks: 94 named checks per successful run in `validation_result`, each with expected and actual values; 93 pass, and the one open check is warning-only (block-group share, EPA join pending). **Rejected records:** scenario 4 quarantined 5 records with file, member, CSV line, key, rule, column and value (`04_failure_bad_records.log`); zero rejected on clean inputs, and the gate tolerates zero. **Transformation log:** every step writes `rows_in` / `rows_out` to `etl_log` and the run log; the trace of section 7 shows the same rules applied to one record.

5. Execution, scheduling, run identifiers, rerun, recovery

- **Execution** is one command (`python pipeline/etl.py run`), safe to repeat at any time; `status`, `rejected`, `snapshot` read the state back. Exit codes and per-gate recovery: Week 7 §6.
- **Scheduling.** The sources change at most once a year (the 2024 Final file), so the pipeline is run on demand rather than on a timer, and that is a documented decision (Week 7 §9). Automation exists where change actually happens: **GitHub Actions runs the whole test-and-scenario suite, plus both record traces, on every pull request and every push to `main`.** If a schedule is ever wanted, the one-liner for Windows Task Scheduler is `schtasks /Create /SC MONTHLY /TN ped_safety_etl /TR "python <repo>\pipeline\etl.py run"`.
- **Run identifiers and logs:** every run gets `run_id` in `etl_run`, carried on every line of `logs/run_NNNN_<start>.log`, every `etl_log`, `validation_result`, `source_file` and `rejected_record` row.
- **Rerun and recovery tests:** scenarios 2 (rerun, identical fingerprint), 3 and 4 (two deliberate failures, tables unchanged), 5 and 6 (kill inside the load; restart closes the abandoned run) — recorded in `docs/evidence/week7_synthetic/` and re-run by CI.

6. Trace of one normal record and one edge case

New this week: `pipeline/trace.py` follows one record through every hop and quotes the evidence — lineage (run, file, SHA-256, release), the record's own CSV lines inside the zip with line numbers, each cleaning rule next to its effect on this record, the stored rows and their constraints, the items contributed to `v_ped_transactions` (or the scope reason it stays out), and the county-rate row the death is counted in. It is read-only and works unchanged on real and synthetic data; `--redact` masks case numbers.

Committed traces (synthetic, against an identical rebuild of the Week 7 scenario load: same six scenarios, same content fingerprint `c0656528b64a…`; CI re-runs both):

- **Normal record** — `trace_normal.log`: a single-victim urban crash; all links resolve; 1 of 2 person rows kept by the unit filter; in the view with 16 items; counted in Volusia's rate.
- **Edge case** — `trace_edge.log`: raw `LATITUDE=77.77770000 LONGITUD=777.77770000` (the FARS "not reported" filler) → stored `NULL/NULL`, no block group possible, walkability item reads `unknown` — and the death is kept, in the view and in its county's rate, exactly as cleaning-plan issue 5 prescribes.

The recorded demonstration repeats both traces on the real files (`--redact` masks the case numbers on screen).

7. Progress against the proposal

Plan of record: the approved proposal's Appendix C week table (Week 3 submission in Canvas), quoted verbatim in the "Planned" column. Status at the end of course week 8:

Wk	Planned (Appendix C)	Delivered	Status
3	Proposal; download all raw files; checksum manifest	Proposal approved; all six files downloaded 2026-09-27, SHA-256 manifest	✔ done
4	Profiling and missingness report; schema, ERD, draft dictionary	Conceptual model, ERD, sample records, business rules (profiling moved to W6)	✔ reordered
5	Ingestion and cleaning scripts; code_lookup; first load	Full physical design: 15 tables (16 since W7 added `rejected_record`), code_lookup seeded, data dictionary, 56 constraint tests	✔ reordered
6	Validation suite, logging, reconciliation; EPA + Census loads; spatial join. **Milestone 1: database v0.1**	Measured profile of the raw files + evidence-based cleaning plan	✔ reordered
7	Analysis view; discretization; baseline frequency tables	Validated, logged, rerunnable pipeline + failure/recovery evidence + CI (view and discretization were already built in W5; baseline frequencies measured in W6 §2.4)	✔ ahead/behind swap
8	FP-Growth mining; redundancy and template filters	This midpoint package; trace tool; real-data run recorded	◐ mining not started

Net position. Milestone 1 (a working, validated database and pipeline) is effectively reached, two items short of the letter of the plan: the **EPA block-group join** (deferred in W7, stage exists and logs itself skipped) and the **real-data load**, whose first execution is this week's recording. The analysis inputs the mining needs (transaction view, fixed bins, baselines) have existed since Weeks 5–6, so mining starts ~2 weeks behind Appendix C with its inputs already in place. Milestone 2 (final rule set) moves from Week 9 to Week 11.

Changes to the plan, as documented in the graded weekly submissions: the Week 4–6 content order was rearranged to match the course's weekly deliverables (model → design → profile/cleaning plan, instead of profile → scripts → validation); direct textbook citations were removed from the Week 6 plan after instructor feedback (commit `eb78b61`) and methods grounding now sits in a dedicated section (Week 7 §8); the EPA join, planned for Week 6 in Appendix C and re-dated to Week 7 by the Week 6 plan, was declared deferred in Week 7 §9 and is scheduled for Week 9 here (risk 2, §9). The question, sources, unit of observation, ethics rules and mining design are unchanged from the approved proposal.

8. Prioritized risk register

#	Risk	Likelihood	Impact	Midpoint evidence	Response	When
1	First real-data load surfaces a code the seeds don't label, or a count mismatch	Medium	High	Pipeline green on synthetic only; real files pinned; G3/G5 totals pre-filled from the Week 6 profile of the same files	Run early in W9 (it is also this week's recording). A rejected code follows the written procedure (Week 7 §6.4: seed + migration, rerun); nothing is dropped silently	W9
2	EPA block-group join (only unbuilt stage) slips again	Medium	Medium	Stage logs itself skipped; walkability = `unknown` for 100% of view rows; Objective 1 tolerates ≤10% missing	Implement in W9 (geopandas point-in-polygon, county-digit consistency check per issue 5). Fallback, already in the proposal: county-level population-weighted walkability	W9
3	Mining window compressed (starts W10, was W8)	High	Medium	View, bins and baselines ready since W5–W6, so the two lost weeks were spent making reruns safe, not on inputs	Mining W10, evaluation W11; Milestone 2 re-dated to W11; report drafting starts from the baseline tables in parallel	W10–11
4	Mining returns trivial or unstable rules	Medium	Medium	Not started; filters specified in the proposal	Closed itemsets, template filters, lift ranking, 4-of-5-year stability, permutation baseline, 2024 hold-out — all pre-committed, not tuned after the fact	W10–11

#	Risk	Likelihood	Impact	Midpoint evidence	Response	When
5	NHTSA publishes the 2024 Final file mid-project	Medium	Medium	2024 tagged `Annual Report File` in `source_file`; replace-by-year proven by scenario 2	Written acceptance procedure (Week 7 §6.5); re-run pipeline, re-run hold-out, report both ARF and Final numbers	any
6	Weeks 12–14 compression against the strict Week 14 package deadline	Medium	High	The proposal's calendar ran to Week 16 (buffer in W14, rehearsal and final submission in W15–16); the course ends at the strict W14 deadline, so the buffer is consumed by the final package	Scope guard, decided now: corridor labels and secondary dashboard views are cut first; data quality, rule evaluation and the report are never cut	W12–14
7	Tableau licence limits for the dashboard	Low	Medium	Not started	Plotly Dash fallback named in the proposal; county choropleth + pattern explorer are library-agnostic	W12

9. Revised schedule, Weeks 9–14

Course week (due Sunday)	Work	Gate / milestone
9 (Oct 18)	Real-data load finalized on the local machine, masked evidence committed (`docs/evidence/week7/`); EPA SLD downloaded and pinned; `block_group` load + spatial join implemented with the county-digit check; block-group share check promoted from warning to gate	**Milestone 1 closed: database v1.0, tagged**
10 (Oct 25)	Baseline frequency and pairwise tables from the database; FP-Growth (mlxtend) at the proposal's thresholds; closed-itemset and template filters	candidate rule set
11 (Nov 1)	Four-of-five-year stability, swap-randomization permutation baseline, 2024 hold-out (labelled provisional)	**Milestone 2: final rule set** (was W9)
12 (Nov 8)	County rates and choropleth; pattern explorer with rule-as-sentence rendering; countermeasure matrix draft	dashboard skeleton
13 (Nov 15)	Dashboard completed + planner walk-through test; report draft (~15 pp) with limitations and bias statements	report draft
14 (Nov 22, strict)	Final package: report, presentation, clean-clone rebuild check, final repository tag	**Milestone 3: final submission**

Slack: the dashboard skeleton (W12) and report draft (W13) can swap if mining evaluation spills into W12; the scope guard of risk 6 applies after that.

Sources and AI assistance

- Tan, P.-N., Steinbach, M., Karpatne, A., & Kumar, V. (2019). *Introduction to data mining* (2nd ed.). Pearson. Chapter 2 (data quality), chapters 5–6 (association analysis) — the

methods basis carried through Weeks 6–7.
- National Highway Traffic Safety Administration. (2026). *FARS National CSV files 2020–2024*. https://static.nhtsa.gov/nhtsa/downloads/FARS/
- U.S. Census Bureau. (2026). *County population totals 2020–2025, Vintage 2025*. https://www.census.gov/data/tables/time-series/demo/popest/2020s-counties-total.html
- U.S. Environmental Protection Agency. (2021). *Smart Location Database v3 / National Walkability Index*. https://www.epa.gov/smartgrowth/smart-location-mapping

I used Claude (Anthropic), an AI assistant, to help build the trace tool, assemble this document, and prepare the demonstration plan. The traces in `docs/evidence/week8/` come from the assistant's Linux environment on synthetic data; the recorded demonstration was made and narrated by me on my machine with the real files. The question, scope, plan and all decisions on changes come from my approved proposal and my Week 3–7 work. I reviewed the generated material and I am responsible for the content.
